The Infrastructure Consortium for Africa
Le Consortium pour les infrastructures en Afrique

NILE BASIN INITIATIVE
Initiative du Bassin du Nil

"Financing Water for Growth in Africa"

Dakar, Sénégal

26-27 Nov 2008

REGIONAL RUSUMO FALLS HYDROELECTRIC AND MULTIPURPOSE PROJECT

INFO ON PROJECT PROGRESS

The Infrastructure Consortium for Africa
Le Consortium pour les infrastructures en Afrique

NILE BASIN INITIATIVE
Initiative du Bassin du Nil

RUSUMO FALLS SITE FEATURES

157 km from Kigali

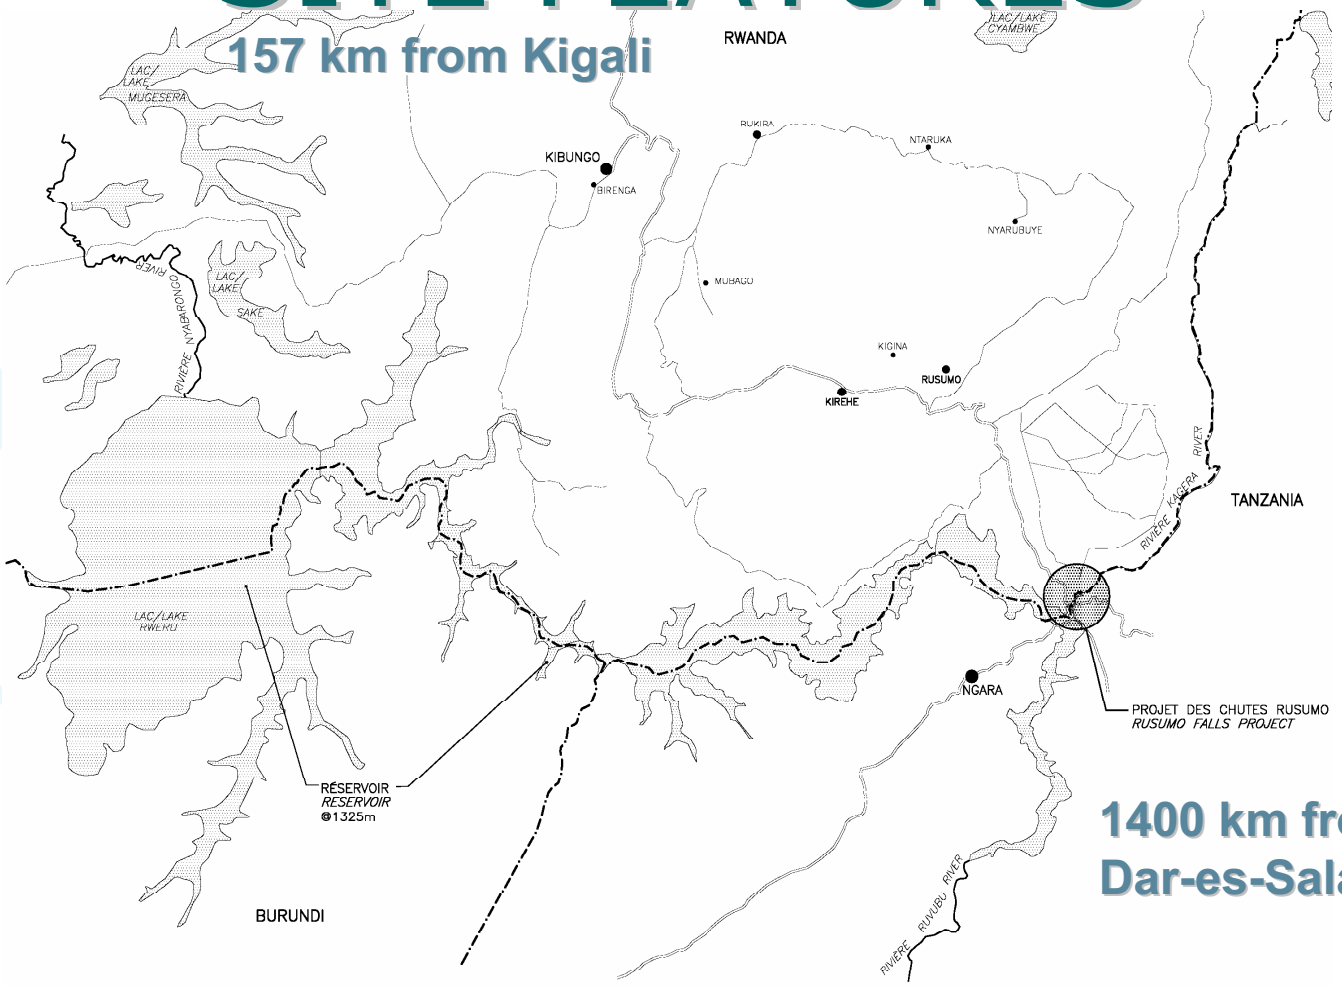

1400 km from Dar-es-Salaam

RUSUMO Falls Location

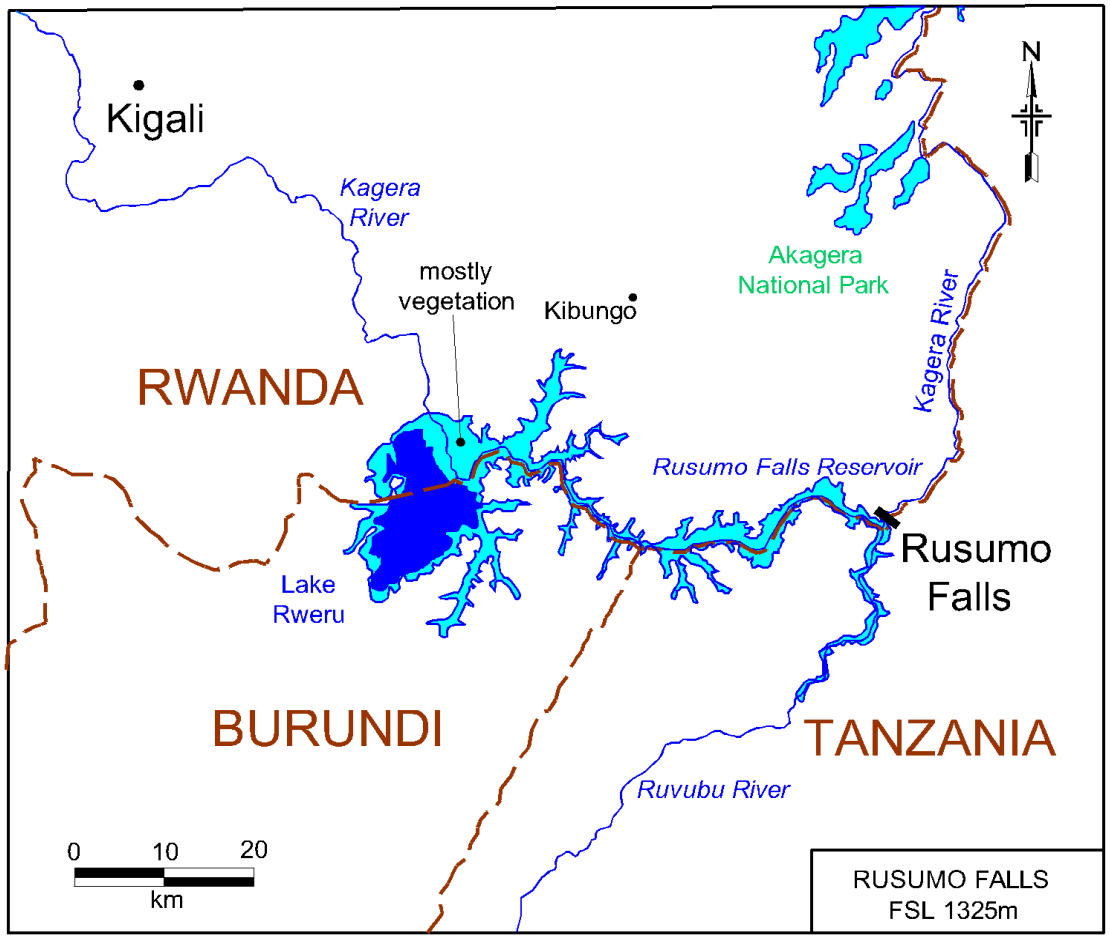

RUSUMO FALLS SITE

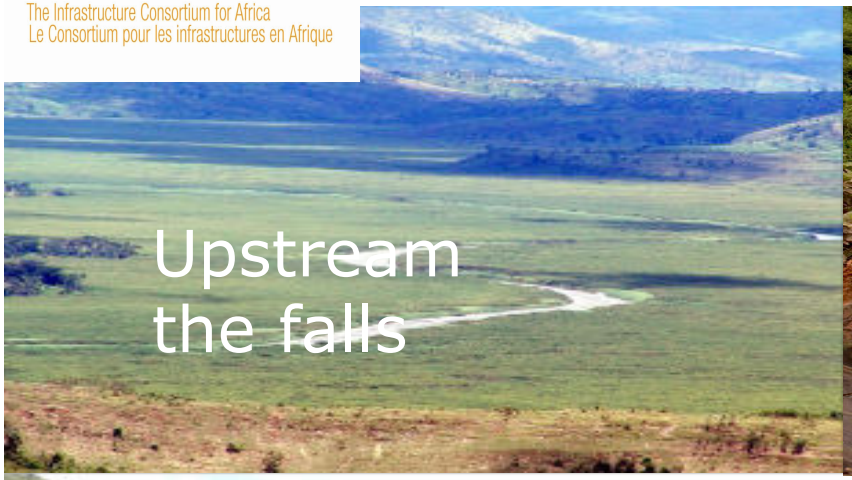

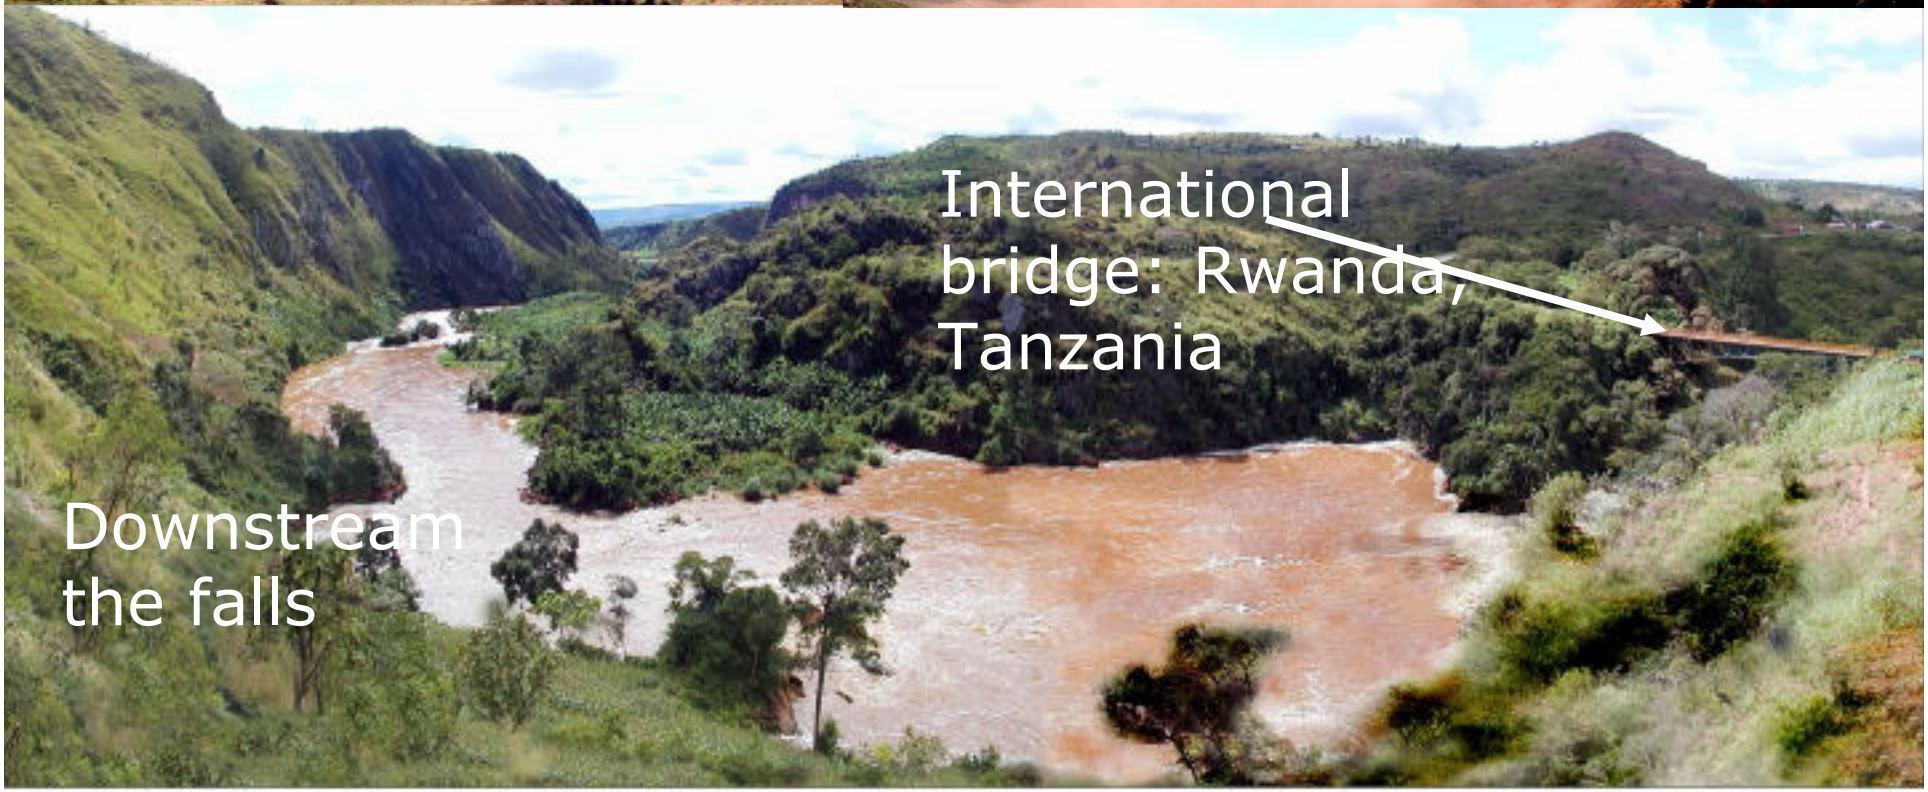

FEASIBILITY STUDY OF POWER GENERATION PLANT AND RELATED PROJECT AREA DEVELOPMENT

- Consultant: SNC LAVALIN, Financing WB
- power generation plant: 60 MW, 3 Kaplan turbines, 444 GWh
- Reservoir capacity at FSL: 496 hm^3
- Reservoir area at FSL: 313 km^2
- Related project area Development included in Project Area Development Plan: public infrastructure (upgrading of roads, school buildings, recreational/tourism facilities), public health (health centers, HIV control, vaccinations, access to clean water, pit latrines, water borne diseases control), socio-economic interventions, agricultural intensification through irrigation, fisheries.

- A joint institutional mechanism for the co-management of power generation and distribution to national utilities will be defined.

- Preliminary Design Report, including ESIA, delivered on 20th November 08.
- Final Design study phase ongoing until End of March 09.

The Infrastructure Consortium for Africa
Le Consortium pour les infrastructures en Afrique

NILE BASIN INITIATIVE
Initiative du Bassin du Nil

STUDY ON THE ELECTRICITY TRANSMISSION LINES LINKED TO THE RUSUMO FALLS HYDROELECTRIC GENERATION PLANT

- Consultant: Joint Venture FICHTNER+RSW I, Financing: ADB;
- Power from the Rusumo Falls will be transmitted to the National grids via three 220 kV transmission lines: Rusumo Falls – Gitega (Burundi), 158 km; Rusumo Falls – Kigali (Rwanda), 115 km; and Rusumo Falls – Nyakanazi (Tanzania), 95 km;
- Rural electrification along the Transmission Lines corridors.

- Prefeasibility Report delivered on 20th November 08.
- Feasibility study phase ongoing, Detailed Design Report and Tender documents awaited End of July 2009.

The Infrastructure Consortium for Africa
Le Consortium pour les infrastructures en Afrique

NILE BASIN INITIATIVE
Initiative du Bassin du Nil

RUSUMO FALLS – COST ESTIMATION

60 MW - $256.9 MILLION

Description	**Estimated Price (M$USD)**
Civil works	114.998
Mechanical & Electrical Works	90.019
Socio-Economic and Environmental costs	32.399
Engineering, Administration & Supervision, Development costs	19.467
Estimated Project Costs	**256.892**

Next steps

- mid -2009: studies completed;
- 2009: financial closure;
- 2010-2013: construction, environmental mitigation and project area development;
- 2013—2014: on power & further Multipurpose investments.

The Infrastructure Consortium for Africa
Le Consortium pour les infrastructures en Afrique

NILE BASIN INITIATIVE
Initiative du Bassin du Nil

THANK YOU

FOR YOUR

ATTENTION !
